

## Construction Update:

- Pile driving for east bridge finished on 11/14.
- 94 piles were installed.
- The piles are typically 86.5' long and 2' dia.
- Rebar installed in piles.
- Concrete piles poured.
- Pump station mostly backfilled.
- Crane has been demobilized.
- Rat Slab poured (base for bridge foundation)


## Construction Photos



Pile Driving, Piles Cut-Off.



Top of East Bridge Excavation, Shoofly Visible.

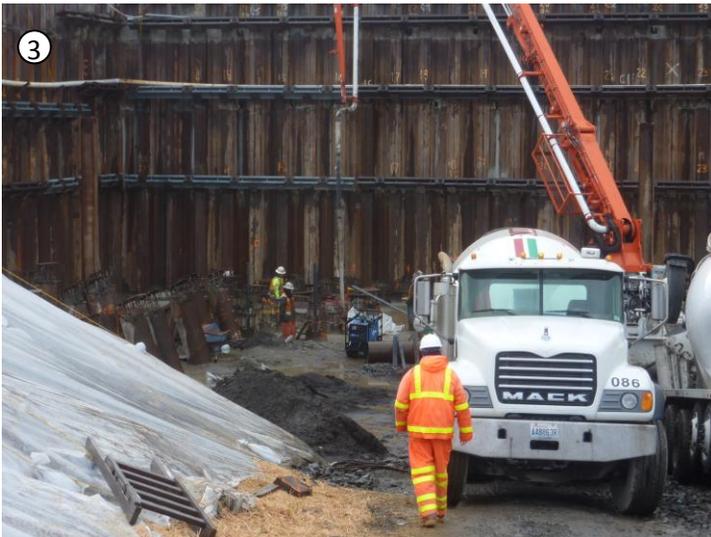

Pouring Concrete in Piles, Rebar Cages Visible.



Top of Installed Wet Well, Valve Vault and Manhole for Pump Station.

For more construction photos, visit the project website <http://rentonwa.gov/living/default.aspx?id=8080> , where there is a link to more construction photos on a City Flickr webpage.
